

Andrews Avenue Drawbridge Rehabilitation Project Update


Summer 2019

Summary

The Andrews Avenue Drawbridge Rehabilitation Project began in July 2018 and is presently on schedule to be completed in March 2020.

Completed Work

- Structural steel components within the bridge pier have been coated with protective paint in the new bridge color.
- Installation of new structural steel elements to reinforce bridge main beams.

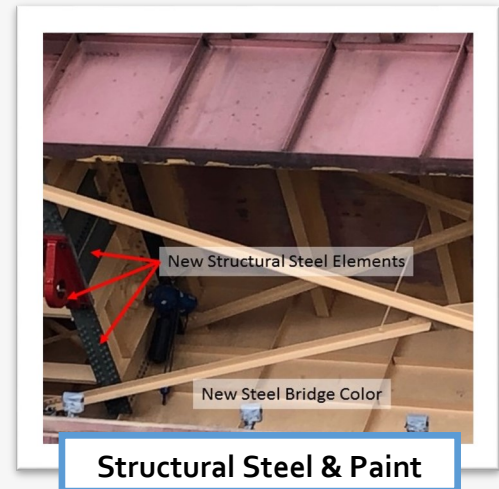


Structural Steel & Paint

Upcoming Work

- Structural repairs and upgrades to the south pedestrian ramp.
- Painting of the structural steel exterior bridge elements.
- 30-day bridge closure to allow existing machinery removal and installation of new machinery and bridge controls.

Work Currently in Progress

- Installation of new bridge traffic and barrier gates.
- Shop-testing of the mechanical, electrical and hydraulic equipment to be installed during the 30-day bridge closure.

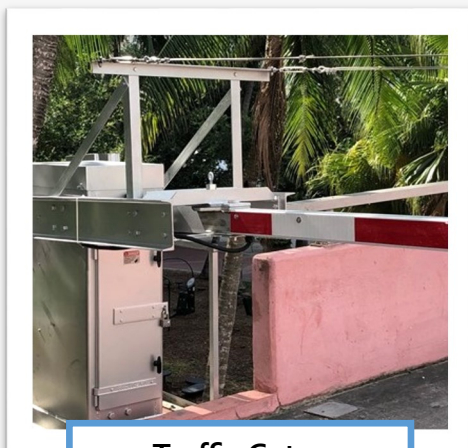

Traffic Gates

Vehicular Impacts

- Until project completion, March 2020, closure of one lane in both directions (southbound and northbound) will be in effect.
- Beginning September 9, 2019: bridge will be closed for no more than 30 days (September 9 through October 8, 2019).

Maritime Vessel Impacts

- Boaters will notice minimal impacts to navigation.

CONTACT:

Project Manager Harry Diaz, P.E., can be reached at 954-577-4631 or 954-931-9067 (cell) or at hadiatz@broward.org. For additional questions, please contact Highway and Bridge Maintenance Division at 954-357-6040.
